

# PENNICHUCK WATER WORKS FLOW TEST


LOCATION Ridge Road DATE 7/18/2008 TIME 2:45am

DISTRICT Nashua REQ. FLOW \_\_\_\_\_ OBSERVER DL

PRESSURES	HYD. NO.	GAGE NO.	OBS.	COR.
STATIC	1		96	96
RESIDUAL	1		72	83

HYD. NO.	GAGE NO.	OUTLET	PRESSURES		DISCHARGE
			OBS.	COR.	
1		2.5"	T=68 S=25	43	1002
2.5" diffuser used Coef of .89 used					
TOTAL					1002

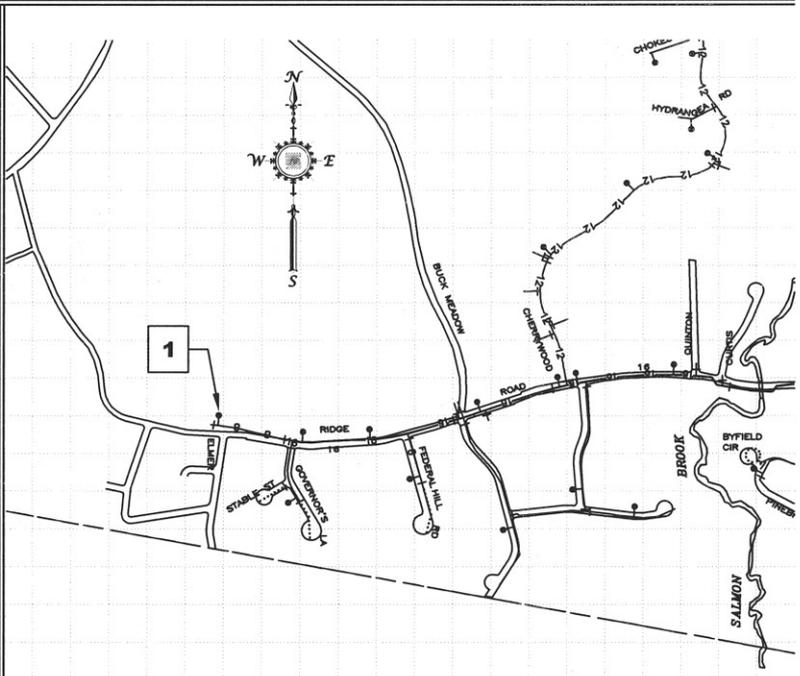

AVAILABLE AT 20 PSI 2602 GPM
